# HSGA Build-Out PLM Roadmap: HR360

Nov 3, 2026 · @jeffrey · Draft

## Summary and decisions requested

The HSGA build-out ships in three releases. MVP1 puts a governed semantic knowledge layer (SKL) under the single HR360 agent by 22 January 2027. The semantic services baseline makes it multi-customer and publishable by 24 May 2027. The agent fabric then puts several governed agents on the same services from mid-2027; those dates are proposed.

Each release advances four workstreams together: the three semantic services, governance across all five domains, the target operating model, and the HR360 agent itself. Persona instances are released with the first keel at week 6.

Decisions requested:

1. Approve the three-release roadmap and its gates.
2. Approve the five governance domains (data, semantic, analytic, AI and trust, decision) as the governance scope, each with a named owner by M-G2.
3. Approve the operating model roles, and seat the governance council by B-G0 on 21 December 2026.
4. Approve the 12 HR360 persona instances and 8 operational personas as the initial catalog, owned by Personas & Jobs.
5. Close the open items before week 1: the 2 to 3 in-scope plans, the HR360 integration path (MCP, per the target architecture), and named team members.

## Scope, starting point and assumptions

The build starts from one agent and one anchor domain, and grows by reuse rather than rebuild.

- **Starting point.** HR360 is a single agent today. Compass is the AI layer; agents are built with Copilot and other LLMs. AI reaches the scaffold through the MCP layer. The scaffold reaches SAP, Salesforce, SharePoint, Workday, PEO products & services and third-party systems through the API layer.


- **Anchor domain.** Employee Benefits & Retirement Sponsorship is modeled in full. Payroll, compliance, client relationship and HR technology enter as slices; talent, workforce development and ethics as references only (Semantic Governance v2.2, Appendix D, Section 2).
- **In scope.** Benefits and retirement questions from worksite employees, client HR administrators, and internal HR and benefits staff.
- **Out of scope for MVP1.** Transactions (the agent explains and points to where to act), personal data (synthetic or de-identified only), and financial, tax or legal advice.
- **Two tracks already planned.** The MVP1 statement of work runs 2 November 2026 to 22 January 2027. The semantic services baseline runs 9 November 2026 to 24 May 2027, paused 21 December to 3 January. Both number their gates G1 onward, so this roadmap prefixes them M- (MVP1) and B- (baseline).
- **Calendar.** Thanksgiving falls in MVP1 week 4; the holidays in weeks 8 and 9. November open enrollment limits benefits SME time in weeks 1 to 4.
- **Proposed dates.** Everything after 24 May 2027, and MVP2 dates, are proposals in this draft for confirmation at M-G4.

## Roadmap at a glance

MVP1 and the services baseline run in parallel from November 2026; MVP2 and the agent fabric follow from February and June 2027.

**Three releases take HR360 from one agent to an agent fabric**

By month, Nov 2026 to Dec 2027 · dashed bars are proposed · diamonds are gates

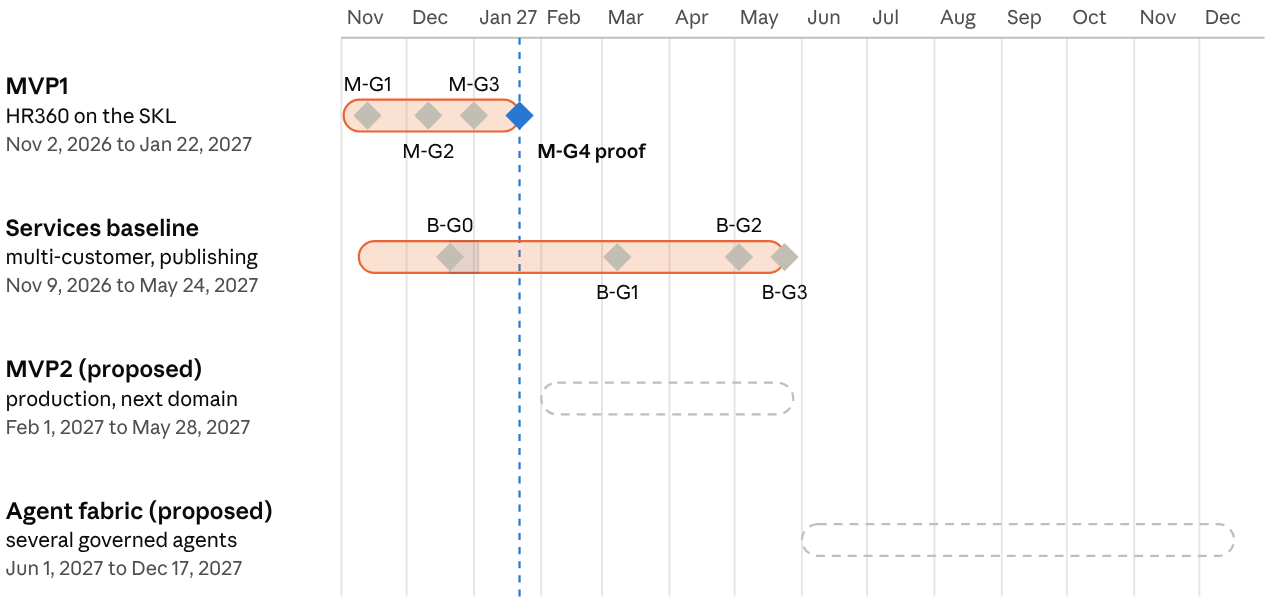


roadmap · 4 releases, 8 gates

The accent line marks the MVP1 proof of capability on 22 January 2027, which also confirms the MVP2 scope. The pale gap on the baseline bar is the 21 December to 3 January pause. Gate criteria are under Measures and acceptance criteria.

## Workstream 1: semantic services

MVP1 configures the existing inbound microservices for benefits and adds six HR360 services. The baseline adds multi-tenant terminology and publishing. The fabric adds one orchestrating agent per tier and a decision gate for every agent.

| Service tier | MVP1: HR360 on the SKL (by 22 Jan 2027) | Baseline: multi-customer and publishing (by 24 May 2027) | MVP2 and agent fabric (proposed) |
|---|---|---|---|
| Inbound | Section 2.6 flow (receive-request to register-asset) for benefits data from Workday/HRScale, payroll codes, recordkeeper feed, client plan selections, plan documents and SPDs, FAQs, regulatory references and de-identified HR360 logs. Orchestration, exception, governance and resilience agents. | Four customer source types (documentation, SharePoint content, data feeds, handbooks) with a tenant tag from the first byte, fail-closed screening and OCR. ESCO releases loaded one at a time. | Production connectors through the API layer to SAP, Salesforce, SharePoint, Workday and PEO products & services. Personal data only under privacy controls. |
| Processing | Mapping registry and mapping-agent; validate-graph against shapes C-01 to C-12; quality, impact, vocabulary and governance agents; extension services; decision-api for rules R-01 to R-14 and calculations K-01 to K-08. New: resolve-persona, classify-intent. | Candidates, matching and triage, lexicon (scoped customer lexicons and extension vocabularies), review state machine, and release with promotion and rollback. | Processing-orchestration-agent; inferencing and learning services (Section 2.7); mapping at scale across the next domains. |

| Service tier | MVP1: HR360 on the SKL (by 22 Jan 2027) | Baseline: multi-customer and publishing (by 24 May 2027) | MVP2 and agent fabric (proposed) |
|---|---|---|---|
| Outbound | Search-gateway facade with query-planning, federation and explanation agents; benefits vector partition (Federated RAG 2.0). New: assemble-answer, grounding-agent, trip-circuit-breaker, record-answer. HR360 calls the facade, never the graph. | Label resolution service on a derived index; publishing contract (publish, validate, reconcile, status, rollback) with the first analytics adapter. | Outbound-orchestration-agent; per-consumer subscription topics; Compass and every agent served through the same MCP tools; a second publishing target. |
| Common | Entitlement filter (R-13) before search; answer trace as PROV-O; release, answer, flag and breaker topics on Kafka. | Policy decision service by persona, job step, resource and context; telemetry from every service. | Decision evaluation for every agent and human decision (pass, comply, freeze, halt) before it takes effect. |

## Workstream 2: governance across the five domains

All five governance domains start in MVP1, each with at least one measured control at M-G3, and deepen with each release. Owners shown are proposed until decision 2 is taken.

| Domain | Proposed owner | MVP1 (by 22 Jan 2027) | Baseline (by 24 May 2027) | Agent fabric (proposed) |
|---|---|---|---|---|
| Data governance | Data steward, Benefits & Retirement | Data classification scheme (Public to Restricted); every digital asset has owner, classification, source and URL (C-08); no personal data loaded; source freshness of one business day or less (RT-17). | Tenant isolation by named graph; fail-closed PII screening with a red-team test; retention rule and written data permission per customer. | Catalog and lineage for every API-layer source; master data for client, worker and plan identities via the identity registry. |
| Semantic governance | Semantic architect, with the governance council | Core, unifying, legal norm and benefits ontologies released v0.5 at M-G2 and v1.0 at week 11; change records for every release (approval traceability 100%); naming and URI rules from Part III. | Lexicon layer beside the core: zero customer-driven triples in the core; label lifecycle and promotion through the council; graph naming by type, tier and name. | Next domain modules reuse the core unchanged; process policies P01 to P09 measured on every snapshot. |

| Domain | Proposed owner | MVP1 (by 22 Jan 2027) | Baseline (by 24 May 2027) | Agent fabric (proposed) |
|---|---|---|---|---|
| Analytic governance | Enterprise Analytics analyst, with the client lead | Measure model; 32 measures (14 design-time, 18 run-time) in the Operations Workbench by week 9; 150-question gold set with a rubric frozen at M-G1; Strategic Outcome scorecard. | Parity tests block any publish where a target's metric differs from the SKL definition; drift per release reported. | Measures per agent and per domain; certification of each new metric before it reaches a dashboard. |
| AI and trust governance | KE lead, with Compliance | Grounding-agent checks every claim; AI circuit breaker trips per domain on RT-02, RT-03 or RT-04 breaches; MTBH measured and trended; ISO/IEC 42001 and NIST AI RMF alignment shown at M-G4. | Policy decisions logged before every read or write; break-glass access time-bound and logged. | Breaker hierarchy from agent to domain cluster to enterprise; topological breakers on fan-out and delegation loops; human-AI teaming controls for reviewers. |

| Domain | Proposed owner | MVP1 (by 22 Jan 2027) | Baseline (by 24 May 2027) | Agent fabric (proposed) |
|---|---|---|---|---|
| Decision governance | Benefits and Compliance SMEs, with the council | 40 SSOT items: 12 constraints, 14 DMN rules, 8 calculations with test vectors, 6 logic flows; versioned parameters with effective dates; advice and escalation policy (R-11, R-12) followed 100%. | Access rules authored in the SKL as governed rules with test cases (nobody approves their own change). | Every agent and human decision evaluated before it takes effect; decision events recorded as triples. |

## Workstream 3: target operating model

The operating model runs live from MVP1 week 9 and adds review, provisioning and simulation in the baseline. Meaning has one owner, the domain steward; everything downstream applies it and never edits it.

**Structure.** A governance council approves releases and cross-domain conflicts. Domain governance teams own meaning and data quality in their domain. The semantic governance CoE runs the platform and the DEV, test, stage and PRD lifecycle.

**One change lifecycle for every asset:** propose, author, review, validate, approve and release, publish, reconcile, learn.

| Role | Accountable for | MVP1 commitment |
|---|---|---|
| Executive sponsor (Enterprise AI Strategy & Solutions) | Direction, gate approvals, removing blockers | Gates and biweekly steering |
| Client lead (Enterprise Analytics) | Outcomes and the scorecard; accepts deliverables | Weekly |
| Senior semantic architect (KE lead) | SKL design, keel integrity, publishing contract, delivery | Full time |

| Role | Accountable for | MVP1 commitment |
|---|---|---|
| Knowledge engineers (2) | Ontologies, vocabularies, taxonomies, mappings, SHACL, SSOT | Full time |
| Semantic services engineer | Microservices, agents, topics, HR360 integration | Full time |
| Data steward, Benefits & Retirement | Labels, definitions, mapping review | 50% |
| Benefits and retirement plan SMEs | Competency questions, gold set, rule and test vector approval | 4 to 6 hours a week each |
| Compliance and Legal reviewer | Legal norms, answer policy, escalation rules | 2 to 4 hours a week |
| HR360 product owner and engineer | Agent integration, feedback signals, demonstration | 25% |
| Enterprise Analytics analyst | Baseline, measures, scorecard | 50% |
| Ops review lead and ops reviewers (from baseline) | Reviewer capacity, service levels, candidate decisions | Sized from the pilot |
| Data and NLP engineers (from baseline) | Source connectors, extraction, matching, gold set | Sized from the pilot |

**Cadence.** Measures reviewed weekly from MVP1 week 6; full set reported at M-G3 and M-G4. Review service levels are set from the pilot, not guessed.

**Operational extensions, by release.** MVP1: Operations Workbench with measures and the run-time issue queue. Baseline: review and data-entry screens, provisioning, monitoring, triage. Agent fabric (proposed): change-impact simulation before every core release.

## Workstream 4: HR360, from one agent to an agent fabric

HR360 moves to the fabric without a rebuild because every stage uses the same services, rules and measures; only the number of agents and partitions grows.

| Stage | Agents | What they share | Controls | Exit criterion |
|---|---|---|---|---|
| Today | One HR360 agent | Nothing governed: answers come from separate content | Not measured | Baseline taken at M-G1 |
| MVP1 (to 22 Jan 2027) | One HR360 agent on the SKL, in test and stage | Search facade, benefits vector partition, decision-api, 12 persona instances | Grounding check on every claim; per-domain circuit breaker; advice and escalation policy; full answer trace | Five demonstration scenarios pass live at M-G4, plus a forced breaker trip and reset |
| MVP2 (proposed, Feb to May 2027) | HR360 in production for Benefits & Retirement; next domain module added | Core and measure model reused unchanged; a second vector partition; routing across domains | Production service levels; personal data under privacy controls | Next domain answers through the same services with only its module and mappings added |
| Agent fabric (proposed, from Jun 2027) | Several domain agents built with Copilot and other LLMs, served through Compass | The same MCP tools, persona model, SSOT and lexicons | One orchestrating agent per tier; every decision gated before it takes effect; breaker hierarchy and swarm controls | Two or more agents answer consistently from one SKL, with traces and measures per agent |

The MVP2 and fabric stages are proposals; the MVP2 recommendation due at M-G4 confirms the next domain and the production path.

# Initial persona instances

Twelve HR360 personas ship in the persona vocabulary at M-G2, and eight operational personas govern who runs the services from the baseline. HR360 personas select relevance, labels, tone and prompt template; they never grant access, and they are set from the authenticated role, never from the prompt.

**HR360 personas** (individuals of core:persona, Semantic Governance v2.2 Appendix D, Section 4.3)

| Persona | User group | Typical needs | Expertise | Channel |
|---|---|---|---|---|
| persona:worksite-employee | Co-employed worksite employee | Eligibility, costs, deadlines, enrollment, own match and vesting | Novice | HR360 agent, employee portal |
| persona:new-hire-employee | Employee in waiting period or first enrollment window | What to choose, by when, auto-enrollment | Novice | HR360 agent, onboarding |
| persona:life-event-employee | Employee with a qualifying life event | Allowed changes and the election window | Novice | HR360 agent |
| persona:departing-employee | Employee leaving or reducing hours | COBRA, final deductions, loans, rollover and distribution | Novice | HR360 agent |
| persona:client-human-resources-administrator | HR contact at the worksite client | Plan offerings, eligibility rules, deadlines, employer obligations | Practitioner | HR360 agent, client portal |

| Persona | User group | Typical needs | Expertise | Channel |
|---|---|---|---|---|
| persona:client-owner-executive | Owner or executive at the worksite client | Plan sponsorship, cost, compliance exposure | Practitioner | HR360 agent, advisor meetings |
| persona:human-resources-specialist | Internal HR specialist or advisor | Complete, sourced answers to repeat and edge-case questions | Expert | HR360 agent, internal search |
| persona:benefits-specialist | Internal benefits operations | Plan rules, carrier terms, enrollment exceptions | Expert | Internal search, HR360 agent |
| persona:retirement-plan-specialist | Internal 401(k) services | Plan provisions, limits, testing, distributions | Expert | Internal search, HR360 agent |
| persona:payroll-specialist | Internal payroll operations | Deduction timing, compensation definitions, corrections | Practitioner | Payroll application, internal search |
| persona:compliance-analyst | Internal compliance and audit | Which norm governs a step; evidence of answers given | Expert | Operations Workbench, internal search |
| persona:insights-analyst | Enterprise Analytics consumer of HR360 measures | Question trends, answer quality, gaps by persona and domain | Practitioner | Dashboards, SPARQL endpoint |

**Operational personas** (proposed in the alternate-labels architecture; catalog owned by Personas & Jobs)

| Persona | Jobs it performs | Works on | From |
|---|---|---|---|
| Tenant provisioner | Create, suspend and remove a tenant; rotate service credentials | Tenant records and graphs, never content | Baseline |
| Onboarding lead | Register sources, confirm data permission, run onboarding reports | One tenant's sources and ingest | Baseline |
| Ops reviewer | Decide candidates, edit labels, raise escalations | Candidates and labels for assigned tenants | Baseline |
| Domain steward | Approve match relations and local concepts; maintain vocabularies, taxonomies, mappings | Assets in the domains they steward | MVP1 |
| Ontologist | Propose ontology, triage-rule and naming changes | Ontology assets, through the lifecycle | MVP1 |
| Platform operator | Run pipelines, releases, rollback and drift response | Services and releases, never content | MVP1 |
| Council member | Approve releases, label promotion, cross-domain conflicts | Release and promotion decisions | Baseline |
| Auditor | Read the audit trail and decision records | Records only | Baseline |

Design-time roles (knowledge engineer, data steward, SME, change reviewer) are operating model roles, not personas. New HR360 personas for the next domain are added in MVP2 through the same change lifecycle.

## PLM lifecycle view

Each release passes the six PLM phases of the assessment scorecard, so the PLM Lifecycle Dashboard can score every release the same way.

| PLM phase | MVP1: HR360 on the SKL | Baseline: multi-customer and publishing | MVP2 and agent fabric (proposed) |
|---|---|---|---|
| Discover | Gold set of 150 SME-approved questions tagged by persona and intent; baseline "before" report (weeks 1 to 2) | Pilot customer, stewards and data permission confirmed; synthetic volumes for the benchmark spike | Next domain chosen from the MVP2 recommendation; agent candidates and their jobs |
| Define | Competency question catalog and ontology requirements (ORSD) by week 2; targets confirmed at M-G1 | Lexicon-layer pattern, five-function service model, benchmark pass thresholds agreed before the spike | Fabric requirements: tier orchestrators, decision events, per-agent measures |
| Design | Core, unifying, legal norm and benefits models; 40 SSOT items; 12 personas | Label record, scoped lexicons, repositories, access rules by persona and job; naming, ID and multi-parent rules at B-G0 | Next domain module; routing and partition design; breaker hierarchy |
| Develop | Keel v0.5 at week 6; inbound mappings by week 7; processing, outbound and six new services by week 9 | Capture, map, manage and serve services; review screens; first publishing adapter | Production connectors through the API layer; MCP tools for Compass and new agents |
| Deliver | Measures live and breaker configured (weeks 9 to 10); SKL v1.0 in stage (week 11); live demonstration at M-G4 | All four source types ingested at B-G1; pilot vocabularies published with clean parity and reconcile at B-G2 | HR360 production release; second agent live on shared services |
| Run | Weekly measure review from week 6; issue queue; breaker trips root-caused within 2 business days | Scale test, second customer onboarded with no core change, runbooks drilled at B-G3 | Service levels per tier; continuous drift and parity monitoring; per-agent MTBH |

# Measures and acceptance criteria

Every gate passes on measured evidence. MVP1 uses 32 measures; the baseline adds isolation and lexicon measures; headline targets are below.

| Gate | Date | Passes when | Approver |
|---|---|---|---|
| M-G1 Baseline | Week 2, 13 Nov 2026 | Competency questions, ORSD, gold set and baseline report approved; targets confirmed against the baseline | Enterprise AI Strategy & Solutions; Enterprise Analytics |
| M-G2 Keel released | Week 6, 11 Dec 2026 | Core, benefits domain, personas and SSOT v0.5 released through the pipeline; competency question pass at least 80%, definitions 100%, SHACL conformance 100%, SSOT test vectors 100% | KE lead; Benefits and Compliance SMEs; Architecture |
| B-G0 Architecture decided | 21 Dec 2026 | Label architecture decided on benchmark evidence; council seated; naming, ID and multi-parent rules agreed; inbound, processing and publishing contracts published | Governance council |
| M-G3 Services live in test | Week 9, w/e 1 Jan 2027 | HR360 answers gold-set questions end to end through the SKL; answer traceability 100% in test; measures reporting | KE lead; HR360 product owner |
| M-G4 Proof of capability | Week 12, 22 Jan 2027 | Five scenarios pass live; after report meets targets or explains each gap; MVP2 recommendation delivered | Enterprise AI Strategy & Solutions; Enterprise Analytics |

| Gate | Date | Passes when | Approver |
|---|---|---|---|
| B-G1 Sources ingested | 8 Mar 2027 | All four source types ingested with provenance; no PII leak in the red team; zero customer-driven triples in the core; zero cross-tenant results | Governance council |
| B-G2 Published | 3 May 2027 | Pilot vocabularies live in the analytics target with clean parity and reconcile checks; pilot lexicon published for its tenant | Governance council |
| B-G3 Scaled | 24 May 2027 | Scale test passed; second customer onboarded with no core change; second target live; runbooks drilled | Governance council |

Headline targets at M-G4 (from the statement of work, confirmed at M-G1): answer accuracy on the gold set at least 90% and 20 points above baseline; hallucination rate below 2%; grounded claims at least 98%; answer traceability 100%; advice and escalation policy followed 100%; zero entitlement violations; 95th-percentile answer time 8 seconds or less; first-contact resolution up 15 points; plan or rule changes reflected within one business day of approval; 100% of the core reused unchanged by the next domain.

## Risks, dependencies and open decisions

The largest schedule risk is SME time in November and December, when both tracks need the same benefits experts.

| Risk or dependency | Effect | Mitigation |
|---|---|---|
| Benefits SMEs are busy with open enrollment and the holidays | Gold set and rule approval slip | Gold set fixed by week 2; holiday weeks used for build work that needs no SME |

| Risk or dependency | Effect | Mitigation |
|---|---|---|
| Both tracks draw on the same team from 9 Nov 2026 | Baseline design competes with MVP1 delivery | Baseline work before B-G0 limited to architecture decisions and the benchmark spike |
| M-G3 falls on 1 Jan 2027 | Gate review cannot be held that day | Hold the M-G3 review on 4 or 5 Jan 2027 |
| Plan provisions vary by worksite client | Rules multiply; answers apply to the wrong plan | Parameters keyed by plan and plan year; MVP1 limited to 2 to 3 plans |
| Source access or tooling arrives late | Weeks 3 to 7 compress | Week 1 access checklist owned by the sponsor; synthetic data fallback |
| Answers read as advice | Compliance exposure | R-11 and R-12, Legal review of the answer policy, policy compliance at 100% |
| Analytics target cannot hold tenant-specific names, or its API is not ready | Customer terms do not reach the target | Publish preferred labels; resolve customer terms in Compass and search; file-based loading as fallback |
| Scope pull from the seven supporting domains | Benefits depth suffers | Depth fixed by scope; additions go to the MVP2 backlog |

### Open decisions

- [ ] In-scope plans (2 to 3) and source systems confirmed (Benefits SME, KE lead; week 1)
- [ ] HR360 integration through the MCP layer confirmed, with a test environment (HR360 product owner; week 1)
- [ ] Baseline source for handle time and escalations (Enterprise Analytics; week 2)
- [ ] Circuit breaker thresholds for grounding, hallucination and MTBH (KE lead, Compliance; M-G2)
- [ ] Owners for the five governance domains (sponsor; M-G2)
- [ ] Approver for the baseline gates B-G1 to B-G3 (shown here as the council; to confirm)
- [ ] MVP2 next domain and the agent fabric start date (sponsor; M-G4)

# Sources


- Semantic Governance: Services, Architecture & Integration, v2.2 draft (1 Nov 2026), Appendix D statement of work and Sections 2.6, 2.7, 3.3 to 3.8
- Architecture Proposal: Alternate Labels and Customer Terminology (31 Oct 2026): semantic services baseline, personas, pilot gates
- DRAFT Proposal: SKL as Single Source of Truth, Publishing into Visier (29 Oct 2026): operating model principles and lifecycle
- Holonic Semantic Governance Architecture v4.2: five governance domains, AI circuit breaker, PLM assessment phases
